

Vernon Trail NLT-0208

Bender Projects

65 South Street Vernon, Indiana 47282

Date Mon 04/07/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

32° 

Snow, Rain, Partially cloudy

Wind: 1 MPH | Precipitation: .0" | Humidity: 96%

12:00 PM

47° 

Rain, Partially cloudy

Wind: 6 MPH | Precipitation: .01" | Humidity: 59%

4:00 PM

56° 

Partially cloudy

Wind: 13 MPH | Precipitation: .0" | Humidity: 47%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 8.30am

Crews of all sorts at commons. Site fairly dry except for runoff to parking area after they arrived from water upstream. Informed Steve Hensley of Friday meeting with David regarding schedule, and concerns regarding overlook drawings and anchor changes, he states office is discussing, but all want to continue to go forth. Concrete crew laying out walk to tie to parking and other pads. Trailer with benches and amenities to be moved to soccer for assembly. Informed Steve of water flow/pressure issue at soccer restroom from weekend.

9.30am

Crew moving to soccer restroom, pulling water meter, obtaining gauges.

11.00am

Ran pressure test at meter, monument shop, hydrant, house, all at 42 pounds. Check internally at restroom and aerator screens all clogged, even after cleaning, lines still show debris. Lights and fan dim when electric water heater turned on. Omara done with checking their work, informed Gary Williams.

12.30pm

Reviewed forming at commons for concrete pour, and limits of 6" for drive, and limits for grass dirt transition behind restroom.

1:00pm

Crew assembling tables. Gary Williams working on purging all restroom lines.

2.00pm

Concrete crews finishing at commons, plan to complete Tuesday, and pour all off overlook, foundation and slab Wednesday. Informed still questions on anchors and drawings. Spoke with Jim Vance regarding beacon volume. Electricians, and plumbing apparently on hold waiting for poole or other determinations. Spoke with David Boswell regarding overlook stamped drawings and anchor changes.

2.30pm

Layed out table and fountain at slab, had to be rotated to 45 for all access.

6.00 pm

Send pics to David of grass rooted and growing in portion of open graded asphalt trail.

Bradley Bender | 04/08/25 | 07:03AM

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey


Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Attachments





04/07/25 | 09:26AM

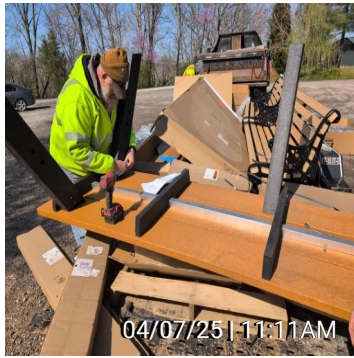

04/07/25 | 11:11AM



04/07/25 | 11:11AM



04/07/25 | 12:29PM



04/07/25 | 12:29PM



04/07/25 | 12:30PM



04/07/25 | 12:30PM



04/07/25 | 12:31PM



04/07/25 | 12:37PM



04/07/25 | 12:38PM



04/07/25 | 12:39PM



04/07/25 | 12:39PM



04/07/25 | 12:39PM



04/07/25 | 12:42PM



04/07/25 | 02:08PM



04/07/25 | 02:08PM




04/07/25 | 02:09PM






04/07/25 | 02:09PM



04/07/25 | 02:36PM

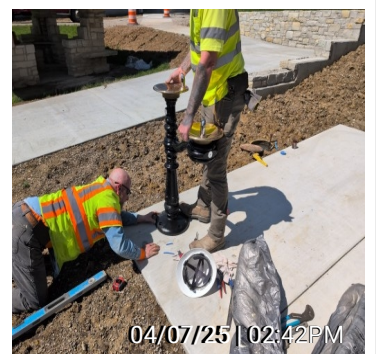

04/07/25 | 02:42PM

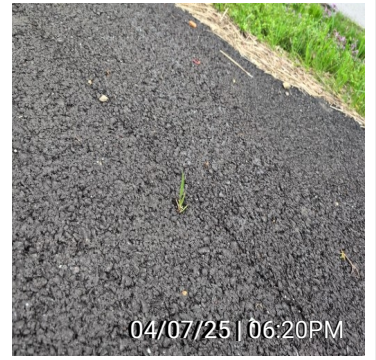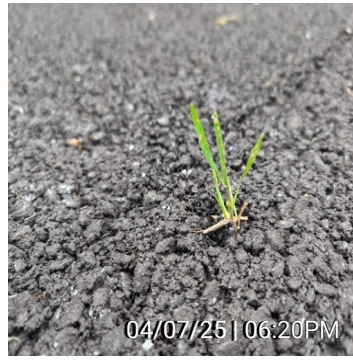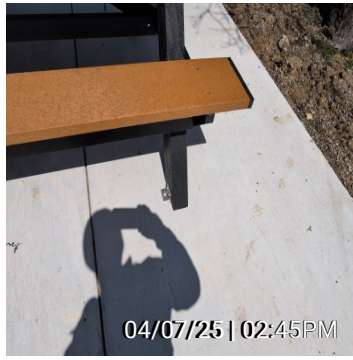

ByBBe

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 04/08/25 | 07:05AM
