

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Tue 04/08/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

29° 

Clear

Wind: 10 MPH | Precipitation: .0" | Humidity: 60%

12:00 PM

35° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 50%

4:00 PM

43° 

Clear

Wind: 0 MPH | Precipitation: .0" | Humidity: 39%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 8.00 am

Concrete crew forming for drive across lift station, scheduled for 11.30am, if the can't get 2 trucks then will finish tomorrow.

Steve attempting to set fountain, advised to rotate with Ada portion towards walk. Lots of debris initial flow, push valve won't close, trying air. Concern that water in pit coming back to fountain from drain valve. Turned off soccer fountain due to temps, that pit is dry, but can't tell if it is draining.

9.00am

Phone with David Boswell, poole questions operable shutters. Koch hit rebar drilling for carriers and chipped black that will need repair, photo sent. Still looking for stamped drawings for overlook and stamped change for anchors. If proceed will be at risk, with deduct for stamped, and long term warranty. All 11th hour discussion.

Also discussed fountain drain back and pits, for punchlist, possibly change to 2nd ball valve.

Noon

Photos of core drills and blowout, rebar in place but no grout in interior walls.

Marked all bollards with Jim and Steve, should be set 13 of 14 removable, 1 to keep, install 57 of 63 delivered, out of original 70. Recommended and accepted 16" core holes over proposed 16 x 16 box cut with demo saw, as legs from saw cuts in concrete or asphalt would require 2 types of sealing, and long term maintenance. Bollards outside the trail will also be cored, but many of the bollards outside of the trail will

need to be hand dug due to utilities.

3.00pm
Rotated fountain for better access, and will add pour to tie to walk. Fountain slab 1/2" low?
Bradley Bender | 04/10/25 | 07:06AM

Site Safety Observations

No entry


Quality Control Observations





No entry

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2. Any schedule delays occur?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3. Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4. Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5. Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6. Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Attachments

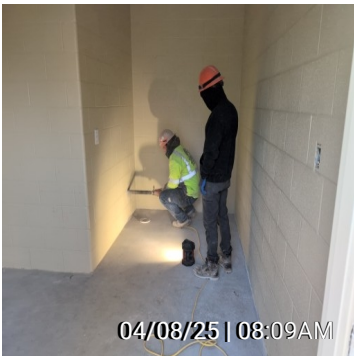

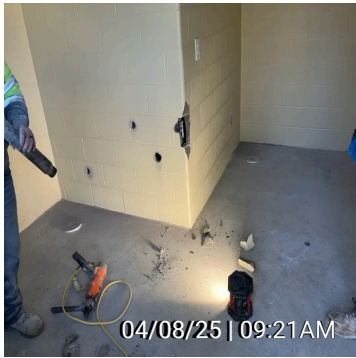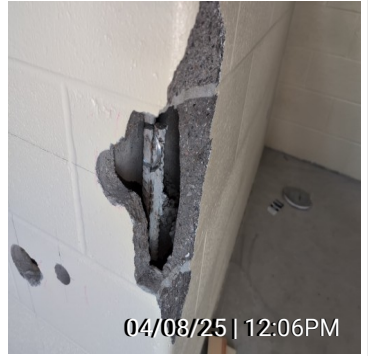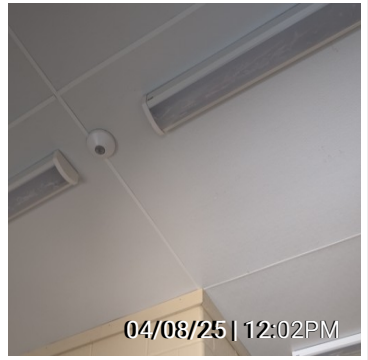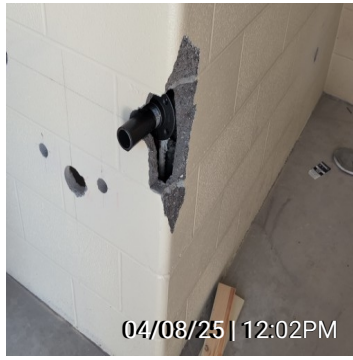

BfB

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 04/10/25 | 06:54AM
