Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Date Wed 04/09/2025

Job#

Prepared By Bradley Bender









6:00 AM Clear Wind: 4 MPH | Precipitation: .0" | Humidity: 79% | Wind: 13 MPH | Precipitation: .0" | Humidity: 42% | Wind: 8 MPH | Precipitation: .03" | Humidity: 66%

		Work Logs		No entry
Name	Description		Quantity	Total Hours
Total			0	0

General Notes

1. 7.30am

Crews layout and excavating overlook. County had not been contacted for inspection, nearby for soccer restrooms, looked at subgrade, and will be back tomorrow at 8.30 prior to 9.30 pour.

8:30am

Phone with David regarding locks at restroom. Center walls at restroom have rebar, but not routed cores, prefer deduct over redo. Savings discussed on bollards not supplied, and supplied but not installed should offset proposed extra for capstone. Informed no stamped drawings for overlook, sending email requesting stick built with Indiana stamp to fpbh as well.

10:00am

Crews at overlook, prepping for excavation and forming. No rebar cages planned. Ensured wings of overlook were monolithic to north end of structure. Poole asking about kiosk layout.

11:00am

Crew pouring at Commons. .


Poole crew wrapping bollards. Told should be one removable not installed to remain, 6 full size not installed to remain.

Koch at restroom, suggested vent manifold should be overhead instead of waist high. Also discussed change of bleed valve to ball vale at winterization pit as better solution. Keith will look into changing water

heater from 80amp to 30 or 40.
2:00 pm Forming at overlook will include outside pours to walk though it could be slab only.
Crews placing and raking topsoil.
Pedestrian bridge showed no affect of high river. Water continuous in ditch could be upstream problem. Loose aggregate in east Jackson.
3:00pm Advised crew working at Montgomery to sweep, and sweep east Jackson.
Steve and crew may be heading to rising sun Monday. Bradley Bender 04/10/25 08:22AM

Sit	No entry					
Quali	No entry					
Survey						
Questions	N/A No Yes Description					
1. Any accidents on site today?						
2. Any schedule delays occur?						
3. Did weather cause any delays?						
4. Any visitors on site?						
5. Any areas that can't be worked on?						
6. Any equipment rented on site?						

Attachments

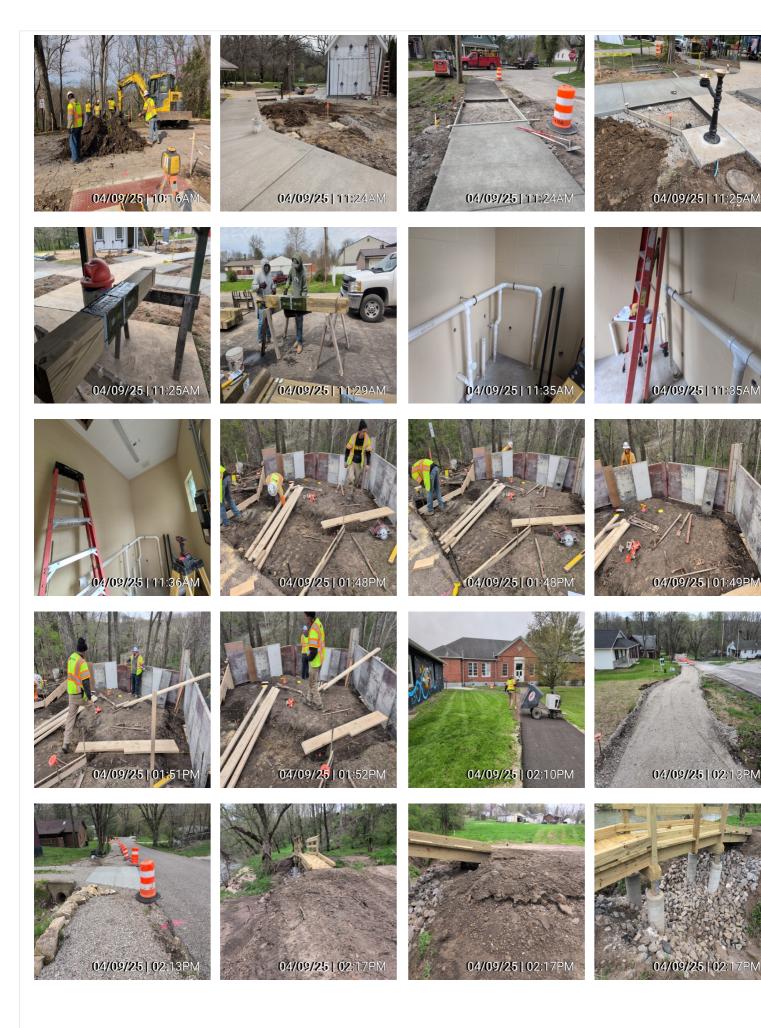



BABL.

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 04/10/25 | 07:01AM
