

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Thu 04/10/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

43° 

Partially cloudy

Wind: 1 MPH | Precipitation: .0" | Humidity: 92%

12:00 PM

56° 

Clear

Wind: 3 MPH | Precipitation: .0" | Humidity: 67%

4:00 PM

63° 

Clear

Wind: 9 MPH | Precipitation: .0" | Humidity: 47%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

- 7.30am
Adding stone and reinforcement at overlook.

8.30am
County inspection at Overlook, approved to pour. Other exc crew at Water street.

9.30am
First truck arrives at overlook.


11.30am
Poole group setting kiosk at commons.
Koch plumbing at commons.
Exc crew setting concrete ribbon along limestone curbs.
Painted a few additional bollards.

1.30pm
Water street trailhead reviewed paint one area to saw cut for topsoil.
Ron Hendershot tested ditch flow, low chlorine.
Kiosk set at Overlook.
No pics.
Bradley Bender | 04/19/25 | 07:10AM

Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments

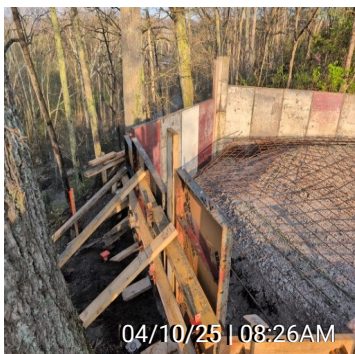



04/10/25 | 09:57AM



04/10/25 | 09:58AM



04/10/25 | 09:59AM



04/10/25 | 10:09AM



04/10/25 | 10:19AM



04/10/25 | 10:19AM




04/10/25 | 10:35AM



04/10/25 | 10:36AM



04/10/25 | 10:47AM

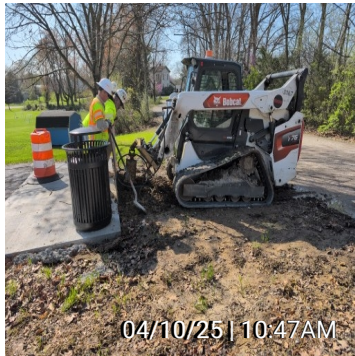


04/10/25 | 10:47AM



04/10/25 | 10:51AM



04/10/25 | 11:12AM

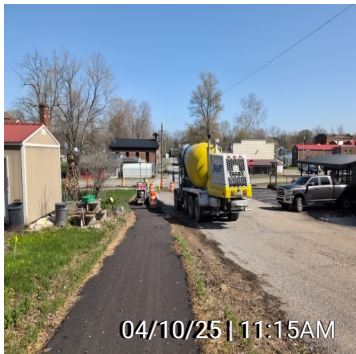

04/10/25 | 11:15AM




04/10/25 | 11:15AM



04/10/25 | 11:23AM



04/10/25 | 11:23AM

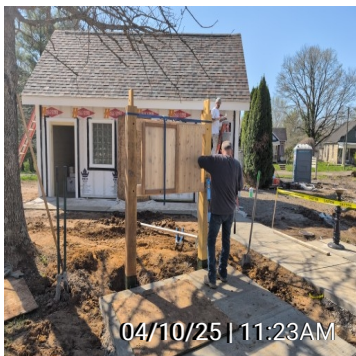

04/10/25 | 11:23AM







04/10/25 | 11:24AM



04/10/25 | 11:26AM



04/10/25 | 11:26AM

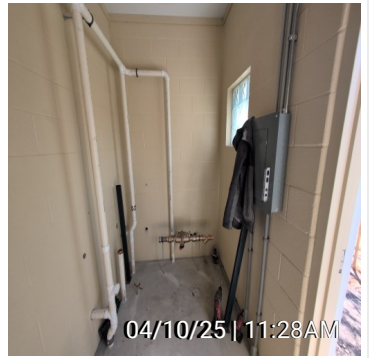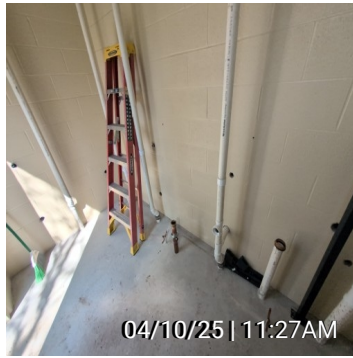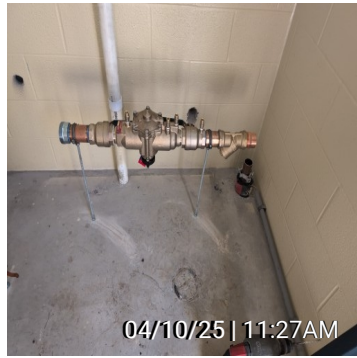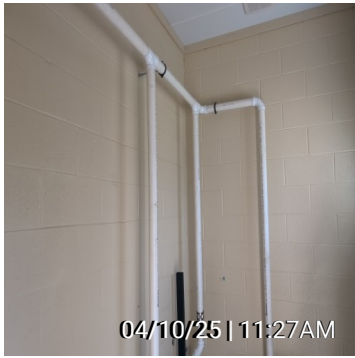

Bradley Bender

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 04/19/25 | 07:10AM
