

Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Bender Projects

Date Fri 04/11/2025

Job #

Prepared By Bradley Bender



Weather

6:00 AM

40°

Overcast

Wind: 10 MPH | Precipitation: .0" | Humidity: 86%

12:00 PM

41°

Overcast

Wind: 13 MPH | Precipitation: .0" | Humidity: 72%

4:00 PM

50°

Partially cloudy

Wind: 13 MPH | Precipitation: .0" | Humidity: 46%

Work Logs

No entry

Name	Description	Quantity	Total Hours
Total		0	0

General Notes

1. 7.30am

Removing forms at overlook, added temporary handrail.

11:00am

Concrete crew filling out day by continuing to cleanup brush below overlook. Exc crew setting limestone curb as barrier and headwall at Jackson at alley. Accepted using 36" deep pieces, and 16 feet to next drive.

1.00pm

Poole setting bollards on East Jackson.

Afternoon.

4 crews everywhere, placing topsoil, and other cleanup in anticipation of seeding Saturday. Staked out bushes and trees with Steve, paint stick stuck on and painted walk at Commons.

Bradley Bender | 04/19/25 | 07:11AM

Site Safety Observations

No entry

Quality Control Observations



No entry





Survey

Questions	N/A	No	Yes	Description
1. Any accidents on site today?	☒	☐	☐	
2. Any schedule delays occur?	☒	☐	☐	
3. Did weather cause any delays?	☒	☐	☐	
4. Any visitors on site?	☒	☐	☐	
5. Any areas that can't be worked on?	☒	☐	☐	
6. Any equipment rented on site?	☒	☐	☐	

Attachments



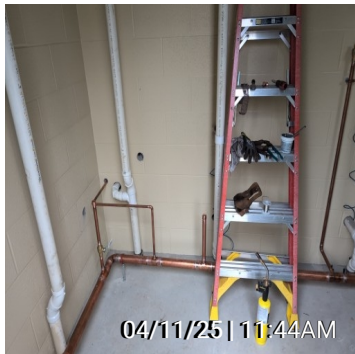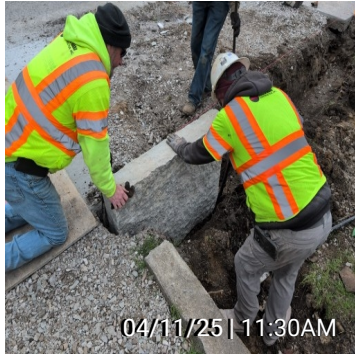

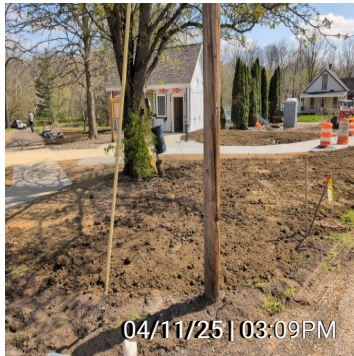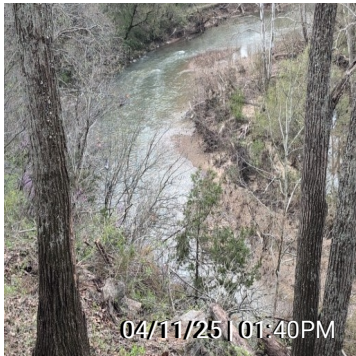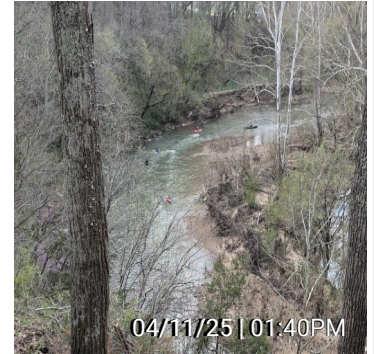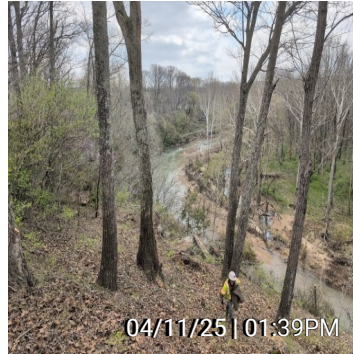

BfBe

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 04/19/25 | 07:11AM
