# Vernon Trail NLT-0208

65 South Street Vernon, Indiana 47282

Date Fri 04/25/2025 Job # Prepared By Bradley Bender









#### 

		Work Logs		No entry
Name	Description		Quantity	Total Hours
Total			0	0

#### **General Notes**

#### 1. 7.30am

About 30 souls from OMara, paving, excavation, clean up, taking out barrels.

AAA layed out for Striping, but drizzled out early. Extra signs delivered, posts will follow later.

4 way stop installed at poplar Jackson. Approved all paint no thermo with credit.

#### Noon

Paving done by noon and pulled out at heavy rain. A cluster of crews all over, some traffic control issues, mostly crowded at school lot.

Poole setting removeable bollards in plates. Locks won't fit.

Koch can't get flush valves to work.

Travis stayed till 3.00pm, reset book box, signs, topsoil, added stone, graded moved out all equipment.

Poole at restroom setting temp locks, still setting partitions after 7.00 pm.

Extra bollards moved to regal building.

Some erosion, runoff issues on west Jackson.

Bradlev Bender | 04/29/25 | 07:30AM

### Site Safety Observations

No entry



Survey				
Questions	N/A No Yes Description			
1. Any accidents on site today?				
2. Any schedule delays occur?				
3. Did weather cause any delays?				
4. Any visitors on site?				
5. Any areas that can't be worked on?				
<b>6.</b> Any equipment rented on site?				

## Attachments



















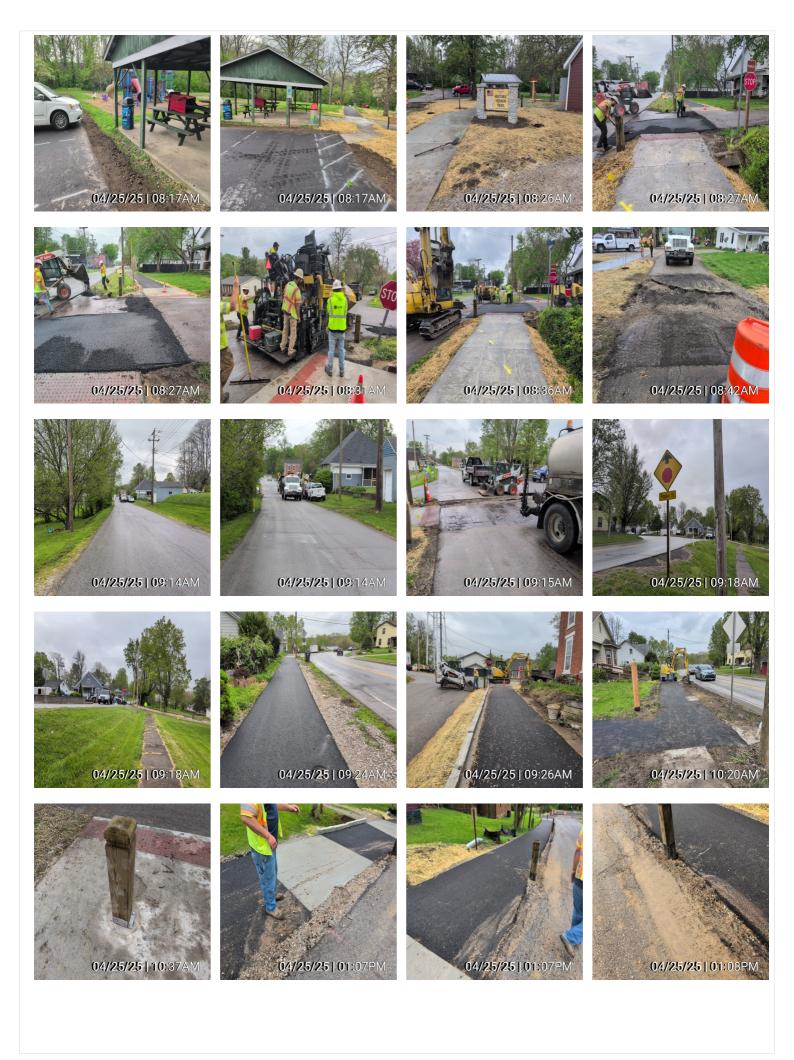



BABL

I, Bradley Bender, have reviewed and completed this report.

Bradley Bender | 04/29/25 | 07:30AM
